Appendix no. 3 - Real property acqusition schedule 3D.2/1 Construction of the right embankment of the Biala River in the City of Tarnów

03/12/2020
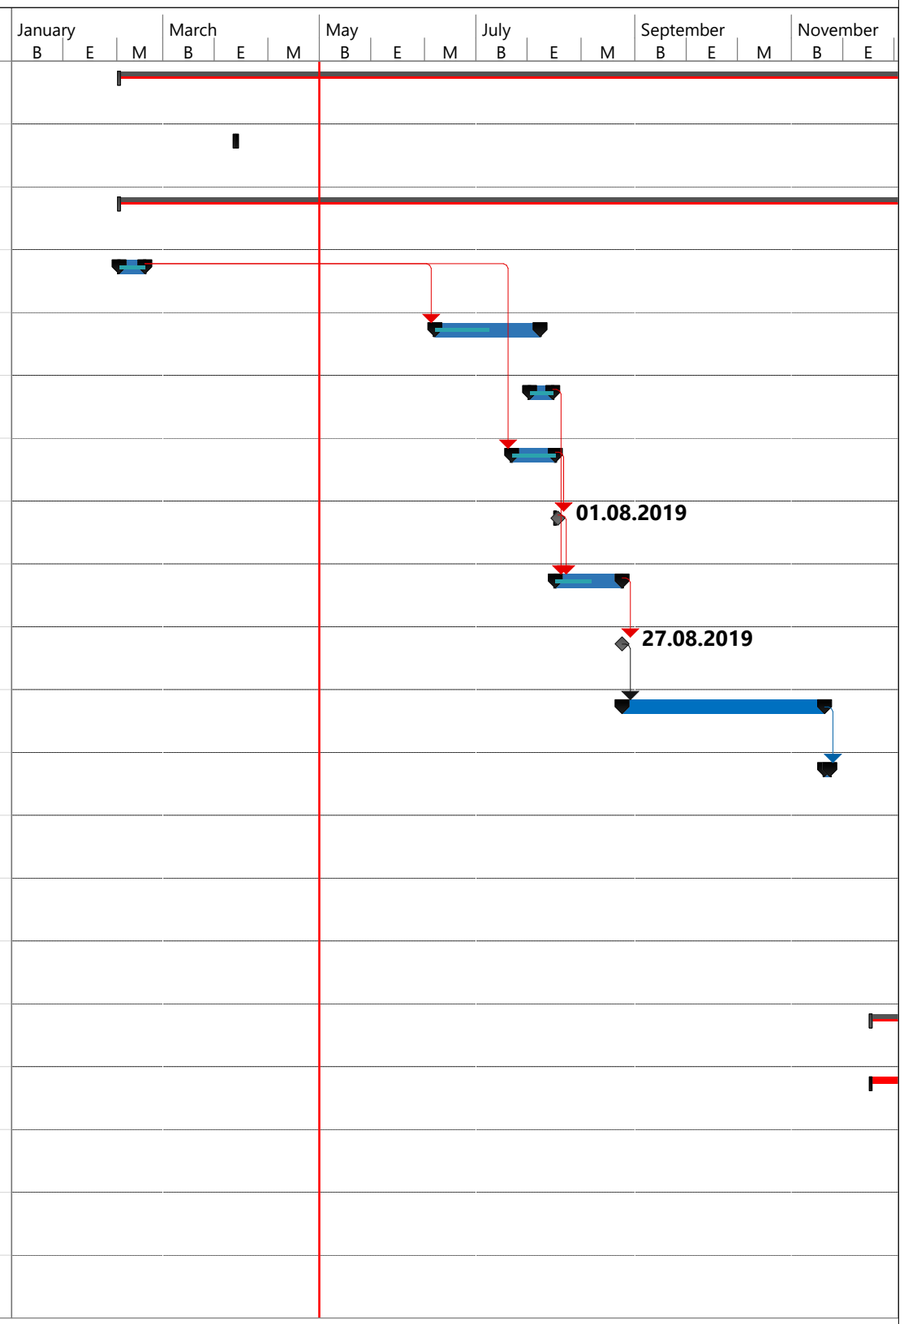
ID	Task	Duration	Start	Finish
1	**3D.2/1 Construction of the right embankment of the Biala River in the City of Tarnów**	**332 days?**	**Tue 12.02.19**	**Thu 21.05.20**
2	Obtainment of the World Bank's "NO" for updated Procurement Plan	1 day?	Fri 29.03.19	Fri 29.03.19
3	**Land Acquisition and Resettlement Action Plan**	**332 days**	**Tue 12.02.19**	**Thu 21.05.20**
4	Identification of the properties necessary for implementation of the project	10 edays	Tue 12.02.19	Fri 22.02.19
5	Socio-economic research	41 edays	Sat 15.06.19	Fri 26.07.19
6	Development of the socio-economic study	9 edays	Mon 22.07.19	Wed 31.07.19
7	Development of LA&RAP	17 edays	Mon 15.07.19	Thu 01.08.19
8	Submission to the Client	0 days	Thu 01.08.19	Thu 01.08.19
9	Client's analyses and updates	26 edays	Thu 01.08.19	Tue 27.08.19
10	Submission to the PCU	0 days	Tue 27.08.19	Tue 27.08.19
11	PCU's analyses and updates	79 edays	Tue 27.08.19	Thu 14.11.19
12	Obtainment of the World Banks' "OK"	2 edays	Thu 14.11.19	Sat 16.11.19
13	Publication of LA&RAP and public hearings	22 edays	Wed 15.01.20	Thu 06.02.20
14	Development of LA&RAP including conclusions of public hearings	35 edays	Thu 06.02.20	Thu 12.03.20
15	Obtainment of the World Bank's "NO"	15 edays	Thu 12.03.20	Fri 27.03.20
16	**Obtainment of properties**	**123 days**	**Mon 02.12.19**	**Thu 21.05.20**
17	Payments of compensation to users of garden plots	87 days	Mon 02.12.19	Tue 31.03.20
18	Issuance of a decision by the Governor on the compensation value	61 edays	Wed 05.02.20	Mon 06.04.20
19	Validation of the aforementioned decision of Governor	31 edays	Mon 06.04.20	Thu 07.05.20
20	Payment of compensation	14 edays	Thu 07.05.20	Thu 21.05.20
